



Rapidset Metal Buildings
 Phone (719) 268-1325
 Toll Free (800) 793-8555
 FAX (719) 599-9382

Mailing Address:
 3555 N Prospect St
 Colorado Springs, CO 80907

CONTACT INFORMATION

Quote ID: **DBS069151** Customer: **Larry Stevens** Date Created: 04/21/2020
 Project Name: Example one Company: Expires: **04/24/2020**
 User: Larry Stevens Phone: State: AR, 71654

STRUCTURAL DETAILS

Est. Building Weight: 7,353

Width: 30' Code: IBC 12 Sidewall Bays: 2 at 20
 Length: 40' Wind Speed: 115 Left Endwall Bays: 1 at 9, 1 at 12, 1 at 9
 Eave L/R: 12/12 Wind Exposure: B Right Endwall Bays: 1 at 9, 1 at 12, 1 at 9
 Slope: 3.0:12 Roof Snow Load: 7 Left Endwall Bracing: Rod Diagonal Bracing
 Load Reduction: No Live Load: 20.00 Front Sidewall Bracing: Rod Diagonal Bracing
 Interior Framing: 1 rigid frame, clear span Collateral Load: 0.5 Right Endwall Bracing: Rod Diagonal Bracing
 Closed?: Closed Back Sidewall Bracing: Rod Diagonal Bracing
 Seismic Zone: C
 Seismic Coef: 0.453

FRAMED OPENINGS

Left Endwall Factory located framed openings: (1) 10 W x 12 H
 Front Sidewall Factory located framed openings: none
 Right Endwall Factory located framed openings: (1) 8 W x 10 H
 Back Sidewall Factory located framed openings: none

FINISH DETAILS

Roof Panel Color: Galvalume Roof Panel Type: 26 Classic Roof (PBR)
 Wall Color: Polar White Roof Screw Length: Long
 Eave Color: Polar White Wall Panel Type: 26 Classic Wall (PBR)
 Corner Trim Color: Polar White Wall Screw Length: Medium
 Gable Trim Color: Polar White
 Jamb Trim Color: Polar White

BUILDING PACKAGE PRICING

Total Building Cost with No Accessories: **\$10,358.75**
 Shipping Included to zip code 71654 (Buyer Will Need To Off Load)
 2 sets of engineered stamped plans included

CHOSEN ACCESSORIES BELOW

Description	Quantity	Cost	Extended
3x7 Full Panel Walk Door - White	1	\$423.66	\$423.66
4" Wall Insulation (R-13)	1	\$1,560.40	\$1,560.40
4" Roof Insulation (R-13)	1	\$1,041.93	\$1,041.93
Insulation Freight (US Lower 48 Only)	1	\$180.00	\$180.00
Total Accessories			\$3,205.99
Total Cost			\$13,564.74
Deposit (30%)			\$4,069.42
Balance Due payable to the first delivery driver			\$9,495.32

202004219230951010


Acceptance of this proposal _____ Date _____

CONTACT INFORMATION

Quote ID: **69151**
Project Name: Example one
Salesman:

Customer: **Larry Stevens**
Company: Larry Stevens
Phone: 719-268-1325

Date Created: 04/21/2020
Expires: **04/24/2020**
Location: AR, 71654

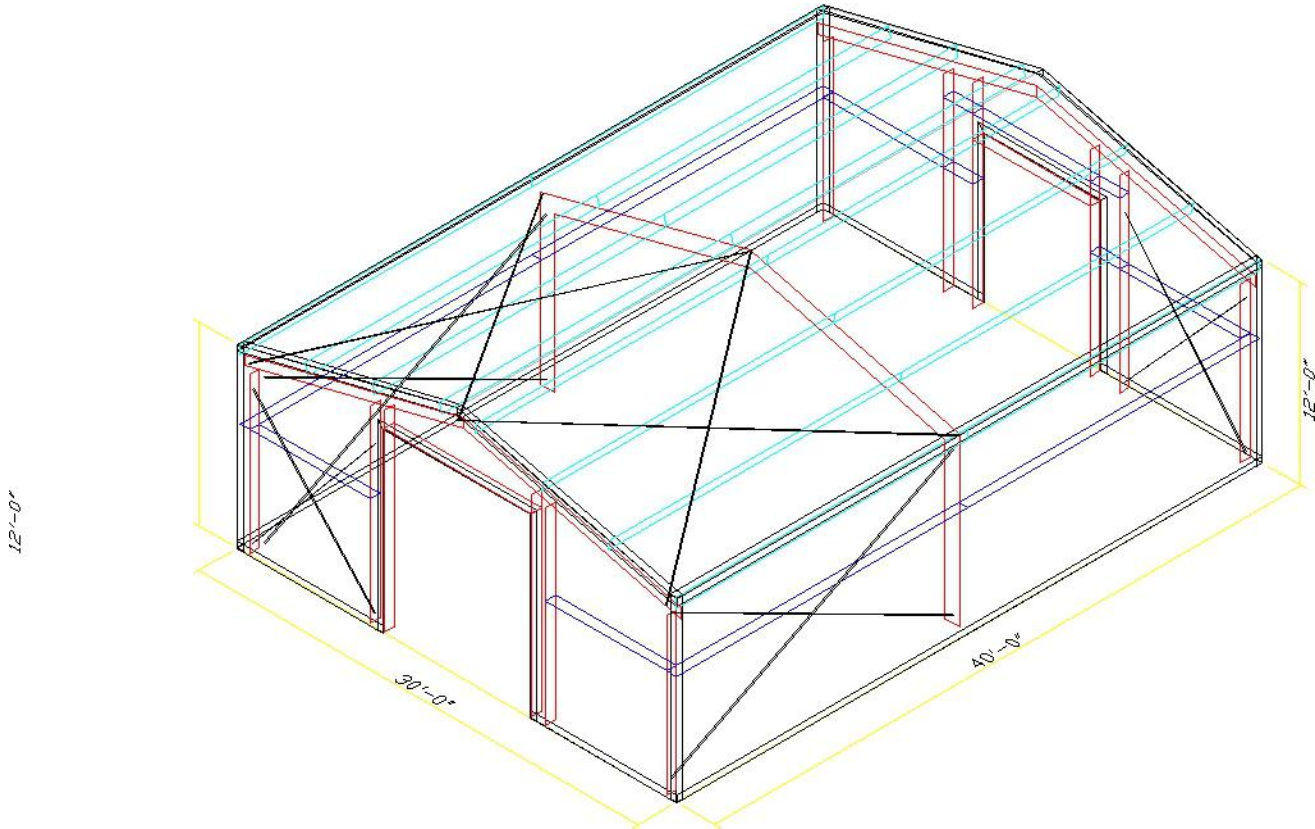

Anchor bolts or fasteners to the concrete are not supplied with this building package unless ordered separately. Sales tax will be calculated at the rate of the delivery address if applicable it will be added to the full payment amount and paid by the buyer when requested. The customer is responsible to check and confirm the loads and codes regardless of our knowledge or conversation during the sales process. If this quote results into entering into a contract to provide this building, once ordered, the buyer is responsible to pay the full amount negotiated and contracted. We recommend that the buyer also hire a professional engineer to design a concrete foundation that will compliment this building. Safety should be considered foremost and can be researched at www.osha.com. We also recommend you plan out the assembly of your building before you start.

We reserve the right to refuse service or sales to anyone for any reason.

Acceptance of this proposal _____ Date _____
